


































































ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	19
1			Gurreb's BBQ	20 wks	Mon 02/02/26	Fri 19/06/26			
2			Hardware and Networking	35.13 days	Mon 02/02/26	Mon 23/03/26			
3			Deploy and configure cloud server	25 hrs	Mon 02/02/26	Thu 05/02/26		Shura Khan	
4			Config web hosting	33 hrs	Thu 05/02/26	Wed 11/02/26	3	Shura Khan	
5			upgrade infrastructure	105 hrs	Wed 11/02/26	Mon 02/03/26	4	Shura Khan	
6			Install hardware	70 hrs	Mon 02/03/26	Fri 13/03/26	5	Shura Khan	
7			Hardware Testing	48 hrs	Fri 13/03/26	Mon 23/03/26	6	Shura Khan	
8									
9			Modual 1: Backend Database	14.13 days	Mon 02/02/26	Fri 20/02/26			
10			Develop	75 hrs	Mon 02/02/26	Fri 13/02/26		Heather Holt	
11			Deploy	9 hrs	Thu 19/02/26	Fri 20/02/26	14	Heather Holt	
12			Unit testing	7 hrs	Fri 13/02/26	Mon 16/02/26	10	Heather Holt	
13			Integration Testing	7 hrs	Mon 16/02/26	Tue 17/02/26	12	Heather Holt	
14			Fixing and regression testing for minor bugs	15 hrs	Tue 17/02/26	Wed 18/02/26	13	Heather Holt	
15									
16			Modual 2: Stock control and inventoy management	13.88 days	Fri 20/02/26	Wed 11/03/26	11		
17			Develop	80 hrs	Fri 20/02/26	Fri 06/03/26		Stephnie Hammo	
18			Deploy	9 hrs	Tue 10/03/26	Wed 11/03/26	20	Viktor Alvarado,S	
19			Unit testing	7 hrs	Fri 06/03/26	Fri 06/03/26	17	Stephnie Hammo	
20			Fixing and regression testing for minor bugs	15 hrs	Mon 09/03/26	Tue 10/03/26	19	Stephnie Hammo	
21									
22			Modual 3: Table management - Orders and billing	10.75 days	Thu 12/03/26	Thu 26/03/26	18		

Project: Mock task 1 ESP
Date: Thu 29/01/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	19
23			Develop	55 hrs	Thu 12/03/26	Fri 20/03/26		Stephnie Hammo	
24			Deploy	9 hrs	Wed 25/03/26	Thu 26/03/26	26	Viktor Alvarado,S	
25			Unit testing	7 hrs	Fri 20/03/26	Mon 23/03/26	23	Stephnie Hammo	
26			Fixing and regression testing for minor bugs	15 hrs	Mon 23/03/26	Wed 25/03/26	25	Stephnie Hammo	
27									
28			Modual 4: User interface	16.75 days	Fri 20/03/26	Tue 14/04/26	18		
29			Develop	79 hrs	Fri 20/03/26	Wed 08/04/26		Viktor Alvarado	
30			Deploy	9 hrs	Mon 13/04/26	Tue 14/04/26	32	Viktor Alvarado	
31			Unit testing	7 hrs	Wed 08/04/26	Thu 09/04/26	29	Stephnie Hammo	
32			Fixing and regression testing for minor bugs	15 hrs	Thu 09/04/26	Mon 13/04/26	31	Viktor Alvarado	
33									
34			Modual 5: Data analysis	17 days	Thu 26/03/26	Mon 20/04/26			
35			Develop	95 hrs	Thu 26/03/26	Tue 14/04/26	11,18	Stephnie Hammo	
36			Deploy	9 hrs	Fri 17/04/26	Mon 20/04/26	38	Stephnie Hammo	
37			Unit testing	7 hrs	Tue 14/04/26	Wed 15/04/26	35	Stephnie Hammo	
38			Fixing and regression testing for minor bugs	18 hrs	Wed 15/04/26	Fri 17/04/26	37	Stephnie Hammo	
39									
40			Modual 6: Customer online booking portal	42.75 days	Fri 20/02/26	Tue 21/04/26			
41			Develop	100 hrs	Fri 20/02/26	Tue 10/03/26	11	Iwan Jones	
42			Deploy	9 hrs	Mon 20/04/26	Tue 21/04/26	44,4,11,18,24,30	Iwan Jones	
43			Unit testing	7 hrs	Tue 10/03/26	Wed 11/03/26	41	Iwan Jones	
44			Fixing and regression testing for minor bugs	15 hrs	Wed 11/03/26	Fri 13/03/26	43	Iwan Jones	

Project: Mock task 1 ESP
Date: Thu 29/01/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks













External Milestone

Deadline

Progress

Manual Progress

Page 2

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	19
45									
46			Testing	12.5 days	Tue 21/04/26	Fri 08/05/26			
47			Create a test plan (every mod)	30 hrs	Tue 21/04/26	Mon 27/04/26	11,18,24,30,36,4	Stephnie Hammo	
48			Intergration test mod 2	7 hrs	Mon 27/04/26	Tue 28/04/26	11,18,47	Stephnie Hammo	
49			Intergration test mod 3 - 4	14 hrs	Tue 28/04/26	Thu 30/04/26	24,30,48	Viktor Alvarado	
50			Intergration test mod 5	7 hrs	Thu 30/04/26	Fri 01/05/26	36,42,49	Stephnie Hammo	
51			Fixing and regression testing for majour bugs	30 hrs	Fri 01/05/26	Wed 06/05/26	48,49,50	Stephnie Hammo	
52			User / Acceptance testing	12 hrs	Wed 06/05/26	Fri 08/05/26	51	Viktor Alvarado	
53									
54			Training	3.5 days	Fri 08/05/26	Wed 13/05/26			
55			Staff training	28 hrs	Fri 08/05/26	Wed 13/05/26	52	Viktor Alvarado	

Project: Mock task 1 ESP
Date: Thu 29/01/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress


Manual Progress

Page 3

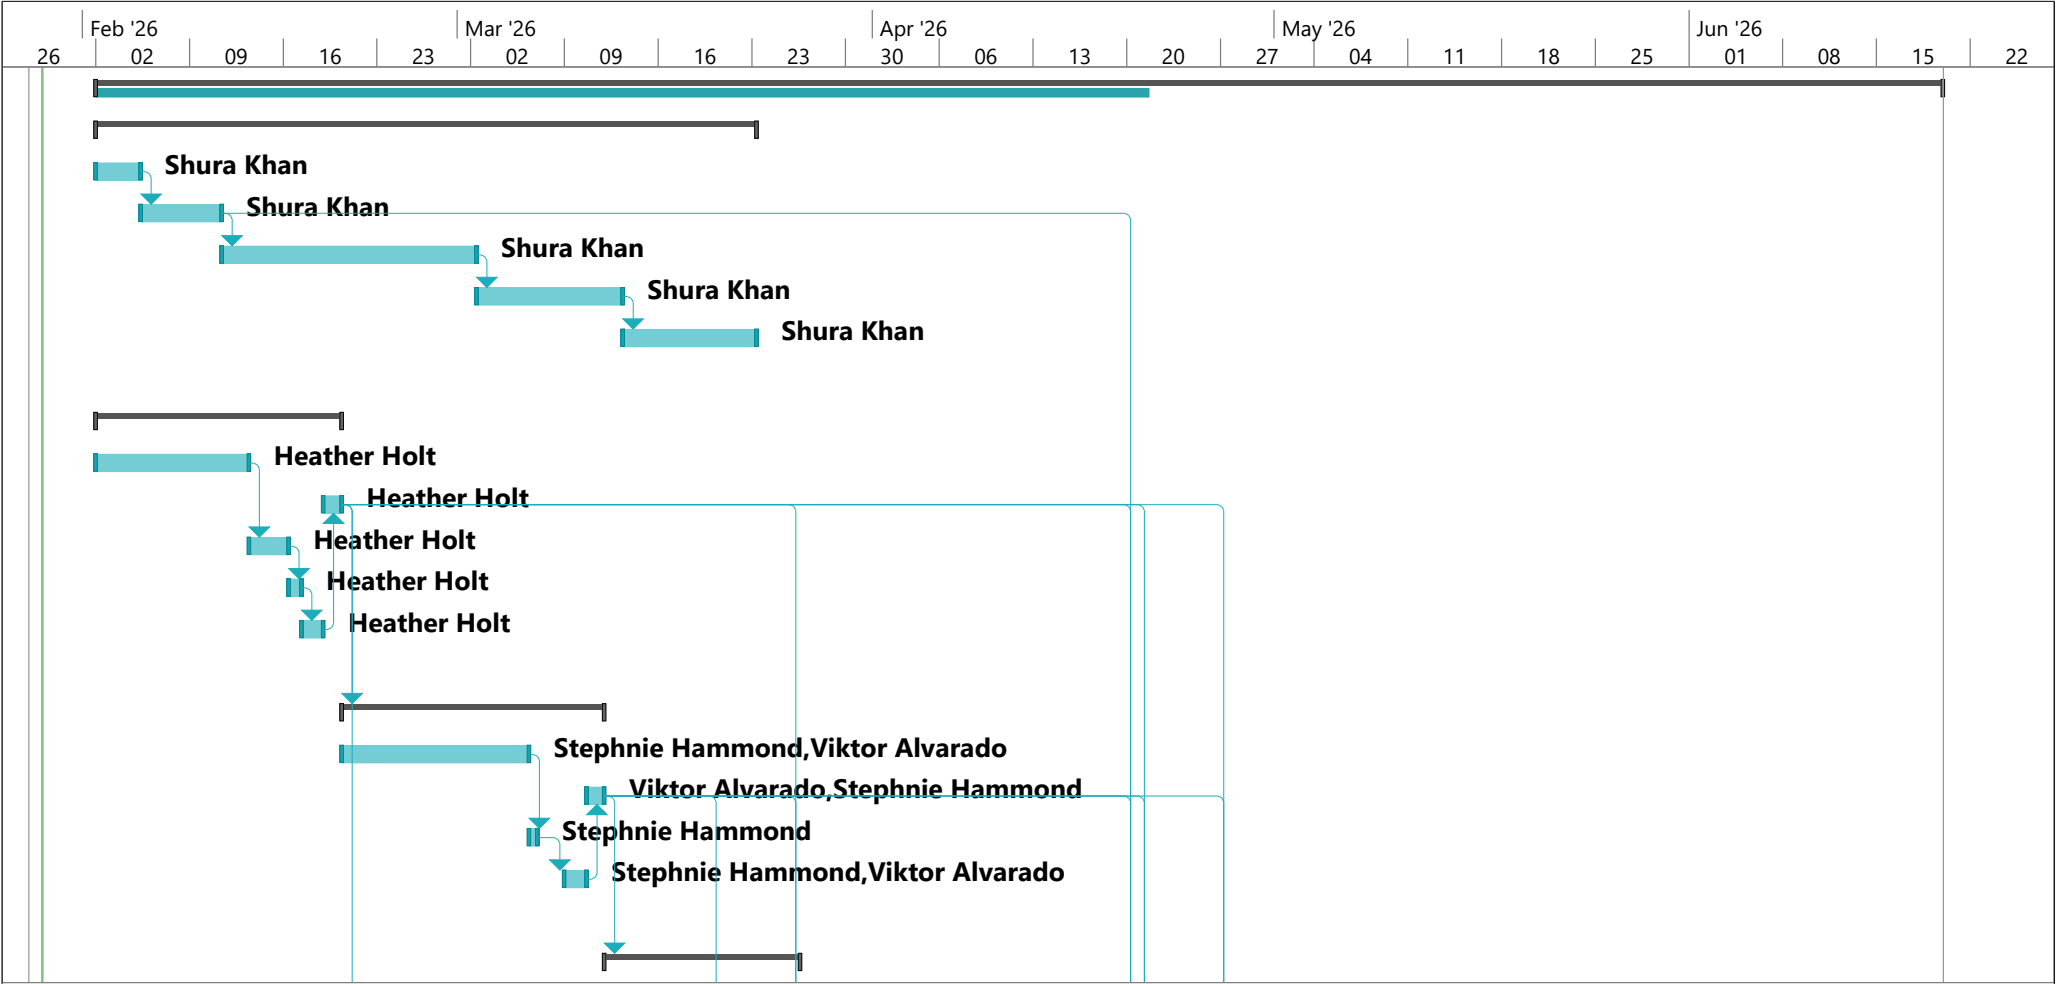


Project: Mock task 1 ESP
Date: Thu 29/01/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

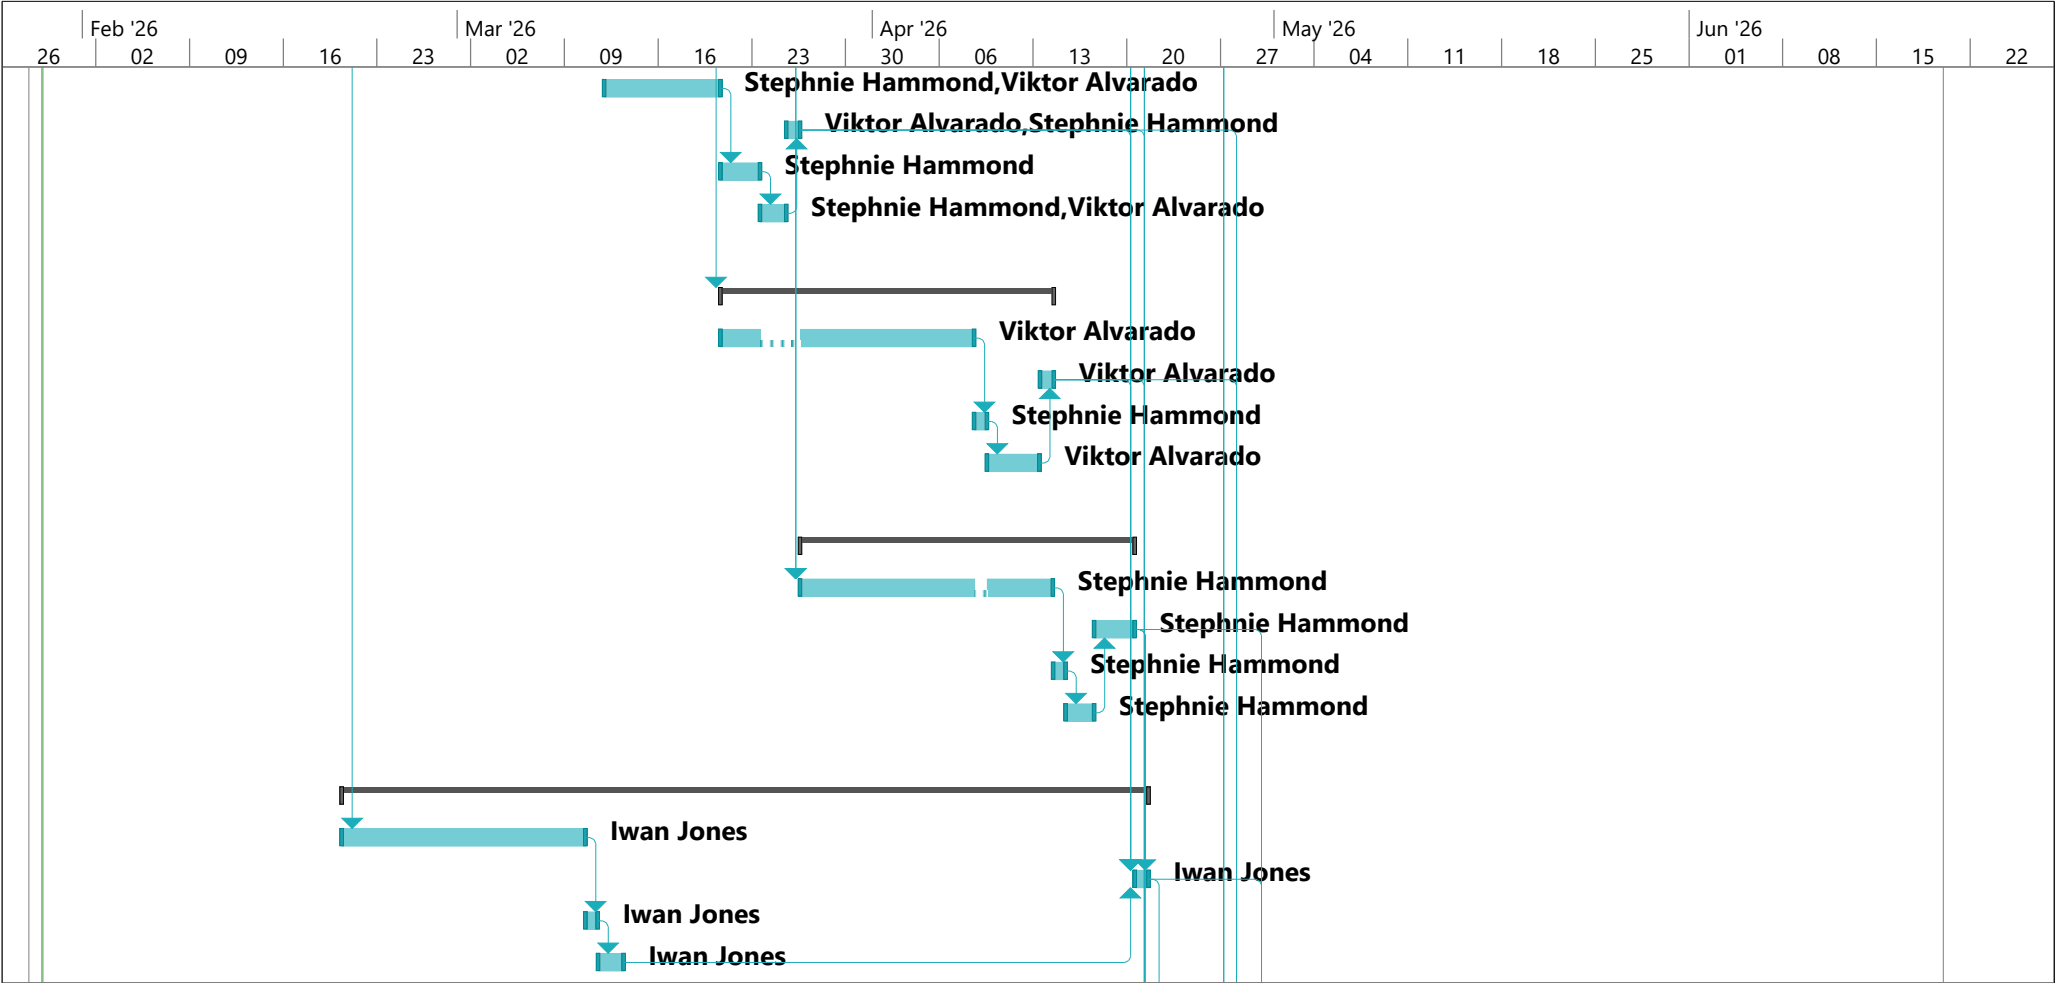

Project: Mock task 1 ESP
Date: Thu 29/01/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

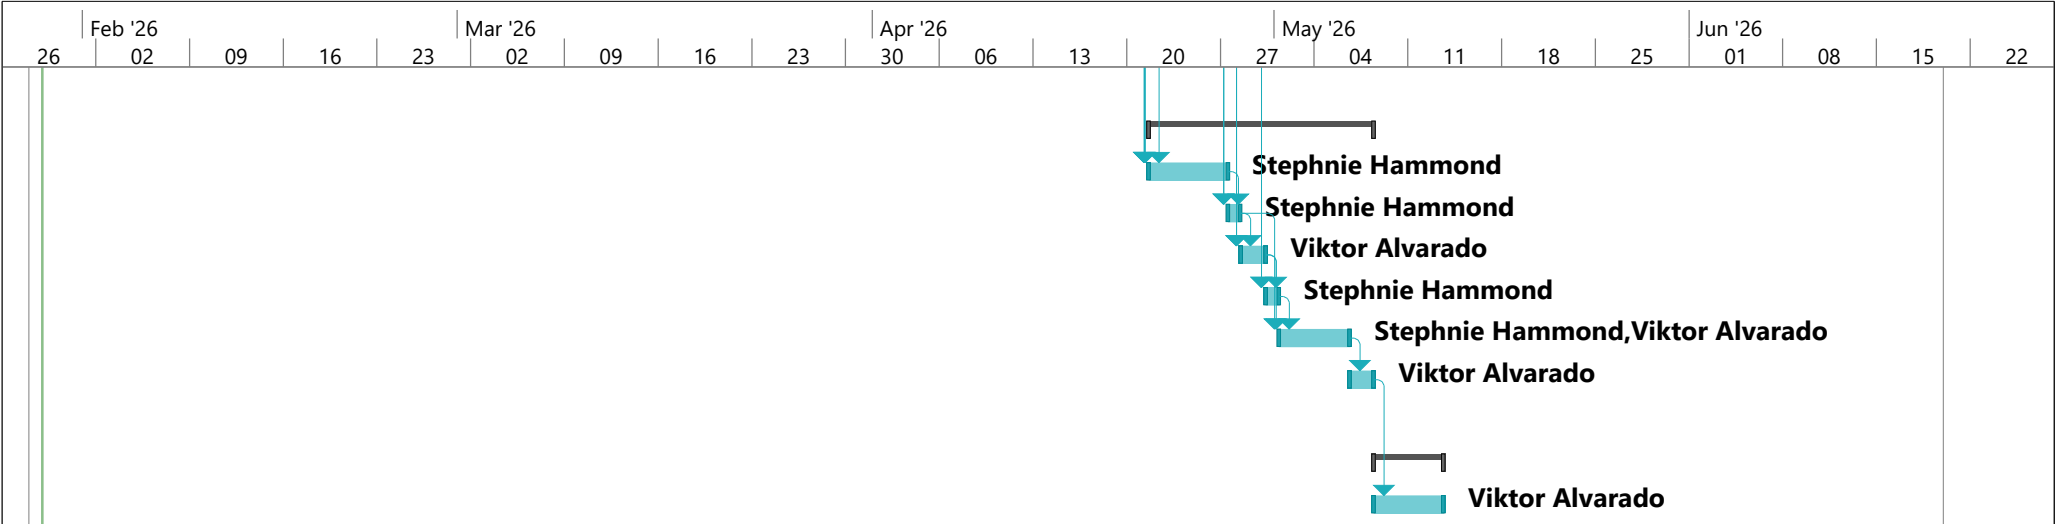

Project: Mock task 1 ESP
Date: Thu 29/01/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

